

FRATERNITI ONE

Franchise Lifecycle Management + Live Reporting System

Software Requirement Document (SRD) + UX Wireframe Pack

Prepared as an implementation handoff for Apoorv and the product/development team.

Product	Fraterniti One
Primary Users	Franchisee, Department Teams, Project Managers, Management
Core Scope	Franchise lifecycle, tasks, documents, approvals, payments, reporting, launch
Design Principle	One franchise. One journey. One source of truth.
Reference Build	Desktop-first responsive web application + mobile responsive views

1. Product Vision and Objective

Fraterniti One is a unified franchise lifecycle operating system that starts when a franchisee signs the Letter of Intent and continues through legal compliance, design, construction, payments, hiring, culinary preparation, marketing, pre-opening, training, launch and post-opening transition. The system must replace fragmented WhatsApp updates, spreadsheets and department-specific trackers with one common project record.

Business objectives

- Give every franchisee transparent real-time visibility into project status and responsibilities.
- Create a single source of truth for every project, task, document, approval, payment and dependency.
- Reduce follow-up effort by automatically generating action queues, reminders and escalations.
- Make the target opening date measurable through readiness scores, critical-path dependencies and departmental sign-offs.
- Give management a portfolio-level command centre for all signed and under-development stores.

North-star experience

At any moment the franchisee must be able to answer three questions: What is happening? What do I need to do? What happens next? Internal teams must be able to answer: Who owns the next action? Is it on time? What is blocking opening?

2. User Roles and Permissions

Role	Primary Access	Key Rights
Franchisee / Owner	Own franchise projects	View status, upload documents, pay/acknowledge, approve/reject, comment
Sales	Sales/onboarding	Create franchise record, upload LOI, commercial handover
Legal	Legal/compliance	Review documents, raise queries, approve legal clearance
Interiors	Design module	Upload versions, manage approvals, freeze design/BOQ
Project Manager	Execution + DPR	Update progress, upload photos, issues, vendors, milestones
Accounts	Payments	Create schedules, verify payment, invoice/receipt status
HR	Manpower	Plan roles, salaries, candidates, joining and readiness
Culinary	Food + equipment	Menu, equipment, crockery, ingredients, trials, training
Marketing	Launch marketing	Campaigns, assets, approvals, launch calendar
Operations	Pre-opening + launch	Readiness, SOPs, training, opening sign-off
Management / Directors	Portfolio-wide	All projects, escalations, analytics, overrides with audit log
System Admin	Administration	Users, roles, templates, masters, integrations, configuration

3. End-to-End Franchise Lifecycle

Stage 01 Sales & LOI -> Stage 02 Legal & Compliance -> Stage 03 Property / Site -> Stage 04 Interiors & Design -> Stage 05 Project Execution -> Stage 06 Accounts (parallel) -> Stage 07 HR (parallel) -> Stage 08 Culinary & Procurement (parallel) -> Stage 09 Marketing (parallel) -> Stage 10 Pre-Opening Readiness -> Stage 11 Training & Trial Runs -> Stage 12 Grand Opening -> Post-opening transition.

Accounts, reporting, communication and document management are horizontal services across all lifecycle stages. A department can work in parallel when dependencies permit; the workflow engine must not force purely sequential execution.

4. Core Functional Requirements

ID	Requirement	Priority	Acceptance
FR-001	Create one Project ID at sales onboarding; all downstream records attach to it.	Must	No department creates a separate franchise record.
FR-002	Show lifecycle stage, progress %, target opening, current master and next action.	Must	Visible on franchisee and internal dashboards.
FR-003	Task workflow with owner, due date, priority, dependencies, status, attachments.	Must	Every actionable item is auditable and searchable.
FR-004	Approval workflow for layouts, BOQ, documents, selections and launch items.	Must	Approve/reject/request change with timestamp and version.
FR-005	Document vault with categories and version history.	Must	Latest approved version clearly identified.
FR-006	CRM payment schedule with due dates, reminders, invoices, receipts and variations.	Must	Payments status updates project/action centre automatically.
FR-007	Opening readiness score derived from mandatory department checkpoints.	Must	100% only when all hard gates are cleared.
FR-008	Critical blocker/dependency engine with impact on target opening date.	Must	Blockers show owner, age, priority and estimated impact.
FR-009	Notifications via in-app first; WhatsApp/email/SMS configurable.	Should	Ready.
FR-010	Full audit log for critical changes and approvals.	Must	Actor, timestamp, old/new value and reference stored.

5. Module Requirements

Sales & Onboarding

- Capture franchisee, brand, format, territory, commercial amount, fee schedule and sales owner.
- Upload signed LOI, payment acknowledgement and commercial proposal.
- Director approval gate.
- One-click handover to Legal; Sales stage becomes locked except authorised amendment.

Legal & Compliance

- Franchise agreement workflow and e-sign status.
- Entity/KYC checklist, GST/PAN/company docs and bank/NACH data.
- Lease/landlord diligence, comments, clause issues and clearance.
- Legal Clearance gate with named signatory and timestamp.

Interiors & Design

- Site measurement record, 2D, MEP, kitchen layout, 3D, material selection, BOQ and design freeze.
- File versioning with V1/V2/V3 etc.
- Franchisee approval/revision comments.
- Approved BOQ can trigger procurement/payment milestones.

Projects / Construction

- Work packages: civil, electrical, plumbing, HVAC, fire, flooring, ceiling, walls, facade, kitchen, furniture, lighting, signage, cleaning, snagging.
- Planned vs actual start/end, % progress, responsible vendor and site manager.

- Daily progress report and photo evidence.
- Milestones and dependencies update overall project progress.

Accounts / CRM

- Project commercial summary and category-wise payout schedule.
- Due, paid, overdue, under verification; invoice and receipt attachments.
- Automatic reminder logic and payment-dependent task unlocking.
- Ledger export and reconciliation-ready fields.

HR

- Opening headcount plan by role.
- Salary range/budget and actual monthly payroll projection.
- Candidate/hired/joining/training status.
- Opening staffing readiness and critical role rules.

Culinary

- Menu, recipes, kitchen equipment, smallwares, crockery, cutlery, glassware, packaging and ingredient/vendor mapping.
- Selection approvals, PO handoff and delivery status.
- Chef/team training and food trials.
- Menu version lock before launch.

Procurement

- Vendor, quotation, PO, value, advance, balance, order, dispatch, ETA, delivery, installation.
- Track all standard categories and custom categories.
- Delay alerts based on required-on-site date.

Marketing

- Google profile, social handles, launch content, influencers, performance ads, local marketing, PR, photoshoot and launch event.
- Asset approval workflow.
- Marketing readiness and campaign calendar relative to opening date.

Pre-Opening / Operations

- Department readiness matrix and hard blockers.
- Licences, inventory, IT/POS, SOPs, training and opening drill.
- Department sign-offs and final Fraterniti Go-Live Approval.

Communication

- Project/department threads, mentions, task-linked messages and attachments.
- Approvals generated from message/task context, not separate WhatsApp confirmations.

Document Vault

- Folder taxonomy by department; metadata, version, owner, status, upload date, approved version.
- Access controlled by project and role.

6. Live Reporting System - Functional Specification

The live reporting layer is not a separate database. It is a reporting and evidence layer over the same project, task, payment, HR, culinary and marketing records. Every update should immediately affect the project status where relevant.

Daily Site Report (DPR)

- Date, project, site manager, weather optional, manpower count by vendor/team.
- Work completed today, planned for tomorrow, work package progress changes.
- Photo/video attachments with upload timestamp; geo-tag support can be added if device permissions are granted.
- Material received, inspections, safety incident, issue/blocker, required decision.
- Submit by configured cut-off; missed DPR becomes an escalation event.

Live Department Reporting

- Each department submits a concise update: completed, in progress, next step, dependency, owner, due date.
- System creates an event feed visible by project and portfolio.
- Reporting compliance displayed as filed/missing by day/week.
- Critical updates can trigger notification/escalation workflows.

Delay & Dependency Engine

- Dependency record links blocked task -> blocking task/person/external party.
- Blocker priority: Critical, High, Medium, Low.
- System stores opened date, age, expected resolution and target-opening impact.
- Critical-path blocker > configured SLA escalates to department head, project head and management.

Management Analytics

- Active projects by lifecycle stage and health.
- Target opening vs forecast opening.
- Milestone on-time %, SLA performance, overdue approvals, payment delays, hiring readiness, procurement risk.
- Portfolio heatmap with Green / Amber / Red / Critical health.

7. Status, SLA and Escalation Model

Object	Recommended Statuses
Task	Not Started, In Progress, Awaiting Franchisee, Awaiting Internal, Blocked, Completed, Cancelled
Approval	Draft, Submitted, Approved, Rejected, Revision Requested, Superseded
Payment	Planned, Due Soon, Due, Under Verification, Paid, Part Paid, Overdue, Waived
Project Health	Green, Amber, Red, Critical

Object	Recommended Statuses
Document	Draft, Under Review, Approved, Rejected, Expired, Superseded
Procurement	Selection, Approved, PO Released, Production, Dispatched, Delivered, Installed, Closed

Recommended baseline escalations

- Payment overdue: immediate Accounts alert + franchisee action card.
- Critical-path blocker open >24 hours: Project/Department Head alert.
- Normal task overdue >2 days: daily escalation until closed.
- DPR not submitted by 7:00 PM local project time: site manager + project head alert.
- T-15 days with readiness below 80%: management escalation.
- Any hard compliance gate incomplete at T-7 days: opening date requires explicit management override.

8. Data Model - Core Entities

Entity	Core Fields / Relationships
FranchiseProject	project_id, brand, format, franchisee_id, location, target_opening, forecast_opening, lifecycle_stage, health
User / Organisation	user_id, organisation, role, permissions, contact, project access
Task	task_id, project_id, module, owner, due, priority, status, dependency, completion evidence
Milestone	milestone_id, project, planned/actual dates, weight, status
Approval	approval_id, object_type/id, version, requested_by/to, decision, comments, timestamp
Document	document_id, project, category, version, file, status, owner, approval_ref
Payment	payment_id, project, category, amount, tax, due, paid, status, invoice, receipt
Vendor / PO	vendor_id, PO_id, category, value, dates, dispatch/delivery/install status
DPR	dpr_id, project, date, manpower, work_done, tomorrow_plan, progress_delta, media, blockers
Issue / Dependency	issue_id, blocked_object, blocking_party/object, severity, age, impact_days, owner
Employee / Hiring	position, required, hired, salary, joining, training, readiness
MarketingActivity	activity, channel, target_date, asset, status, approval
AuditEvent	event_id, user, project, object, action, old/new, timestamp, source

9. Readiness & Progress Calculation

The application should support configuration of weights by brand/format. Recommended principle: overall project progress is milestone-weighted; opening readiness is gate-based. A task being 90% done must not hide a missing mandatory licence or critical hire.

- Project Progress = weighted completion of lifecycle milestones.
- Opening Readiness = weighted department readiness, capped when a hard gate is open.
- Hard Gates examples: franchise agreement, legal/property clearance, essential licences, utility availability, POS readiness, critical staffing, food trial, fire/safety where applicable, final operations sign-off.

- Forecast Opening Date = target date adjusted using overdue critical-path milestones and explicitly estimated blocker impact.

10. Notifications and Automation

- In-app notification centre is mandatory.
- Reminder events: task due, approval requested, payment upcoming/overdue, document expiring, procurement ETA risk, DPR missing, training/re-test due, critical blocker opened/resolved.
- Notification rules should be configurable by event, project and user role.
- CRM/WhatsApp/email/SMS integrations should consume the same event queue; do not hard-code business logic into a single messaging channel.

11. Non-Functional Requirements

ID	Requirement	Priority	Acceptance
NFR-01	Responsive web interface for laptop/tablet/mobile.	Must	Core actions usable at 375px width and above.
NFR-02	Role-based access control and project-level data isolation	Must	Unauthorised users cannot query or download restricted data.
NFR-03	Auditability for approvals, finance and critical statuses.	Must	Immutable event history retained.
NFR-04	Performance: standard dashboards should feel near-instant	Must	Normal browser pagination/caching; target p95 dashboard API <2.5s where practical
NFR-05	File security and signed/authorised downloads.	Must	No public bucket URLs for restricted documents.
NFR-06	Backup, restore and environment separation.	Must	Production data separately protected from staging/dev.
NFR-07	Extensible brand templates and checklist masters.	Must	Add new brands/formats without code changes to every workflow.
NFR-08	Observability: errors, integrations and failed notifications	Should	Admin can identify failed jobs and retry.

12. Suggested API / Service Boundaries

- Auth & RBAC service
- Franchise Project service
- Workflow / Task / Approval service
- Document service
- Finance / Payment service
- Project Execution & DPR service
- HR service
- Culinary / Procurement service
- Marketing service
- Notification / Event service
- Reporting / Analytics service
- Audit service
- Master Configuration service

Apoorv may implement these initially as modules inside a modular monolith if that reduces complexity; the important requirement is clean domain separation and a shared Project ID/event model.

13. Integration Requirements

- CRM: franchise lead-to-project handoff and payment schedule synchronisation.
- Leegality or equivalent: agreement/e-sign status if API is available.
- Petpooja: POS/store data and later operational reporting where applicable.
- Bank/NACH provider: mandate/payment status where integration is approved.
- Cloud object storage: drawings, documents, invoices, site media.
- WhatsApp Business/email/SMS: outbound notifications and action deep-links.

All integrations should be adapter-based. Failure of an external system must not corrupt the core project record; failed syncs must be visible to admins and retryable.

14. Admin & Master Configuration

- Brand/format master and default lifecycle template.
- Department, role, permission and user management.
- Task/milestone/checklist templates with default owner role, SLA and dependencies.
- Payment milestone templates.
- Readiness weights and hard-gate configuration.
- Notification/escalation rules.
- Vendor and procurement category master.
- Document type master and expiry rules.

15. Acceptance Criteria for MVP

- A new signed franchise can be created from sales and handed over without duplicate data entry.
- Franchisee can see status, actions, documents, payments and target opening from one dashboard.
- Legal, interiors, projects, accounts, HR, culinary and marketing can update their own modules.
- A project manager can submit a daily site report with photos and progress updates.
- Franchisee approvals are versioned and auditable.
- Payment due/overdue items automatically appear in Action Centre.
- Opening readiness and blockers are visible to franchisee and management.
- Management can view all projects with stage, health, opening date and owner.
- Critical blockers and overdue items follow configured escalations.
- Every critical update is reflected in the audit log.

16. Recommended Delivery Phases

Phase	Scope
Phase 1 - Foundation	Auth/RBAC, project master, lifecycle, home dashboard, action centre, documents, tasks, audit
Phase 2 - Core Execution	Sales, Legal, Interiors, Projects, DPR, Accounts, approvals, notifications

Phase	Scope
Phase 3 - Opening Ecosystem	HR, Culinary, Procurement, Marketing, training, readiness and launch sign-offs
Phase 4 - Management & Automation	Portfolio command centre, live reporting, dependencies, SLA analytics, integration adapters
Phase 5 - Post-Opening	Operational KPIs, royalty, audits, marketing calendar, franchise health score, support tickets


17. Wireframe Index

The following screens form the first complete design baseline. They are functional wireframes: layout, information hierarchy, actions and state logic are defined; final visual branding can be applied after product validation.

01. Franchise Home Dashboard - Executive franchise status, actions, readiness and lifecycle progress.
02. Lifecycle Timeline - Stage-wise view with completion, current stage and upcoming handoffs.
03. Action Centre - Central queue for payments, documents, approvals and franchisee decisions.
04. Sales & Onboarding - LOI, commercial details, documents and sales-to-legal handoff.
05. Legal & Compliance - Franchise, entity and property compliance workflow with legal sign-off.
06. Interiors & Design - Design versions, approvals, drawings and BOQ lifecycle.
07. Project Execution - Construction work packages, vendors, progress, issues and target dates.
08. Daily Site Report - Live construction DPR with progress, manpower, photos, completed work and next-day plan.
09. Accounts & Payments - Payment milestones, due dates, invoices, receipts and CRM reminders.
10. HR & Manpower - Role-wise hiring, salary planning, joining dates and readiness.
11. Culinary & Menu - Culinary selections, equipment, menu, ingredients, training and trials.
12. Procurement Tracker - Vendor-level PO, advance, dispatch, delivery and installation visibility.
13. Marketing & Launch - Pre-launch marketing calendar, asset approvals and launch readiness.
14. Pre-Opening Readiness - Cross-department readiness score and critical blockers before opening.
15. Training & Certification - Training assignments, assessments, certificates and opening eligibility.
16. Grand Opening Control Room - Final sign-offs, launch-day checklist, team and event readiness.
17. Communication Centre - Department threads linked to project tasks, approvals and files.
18. Document Vault - Version-controlled documents grouped by lifecycle module and department.
19. Management Command Centre - Portfolio view for management: stage, readiness, opening date, health and ownership.
20. Live Reporting Command Centre - Real-time feed, reporting compliance, blockers and cross-department reporting controls.
21. Department Status Matrix - Cross-functional project status with owner, due date, dependency and health.
22. Delay & Dependency Tracker - Critical-path blockers, ownership, aging and opening-date impact.
23. Milestone & SLA Analytics - Stage-wise SLA performance, reporting compliance and escalation rules.
24. Activity & Audit Log - Full traceability for user actions, approvals, edits and system events.
25. Mobile Franchise Views - Responsive quick views for owner actions, site updates and opening readiness.

Wireframe 01 - Franchise Home Dashboard

Executive franchise status, actions, readiness and lifecycle progress.

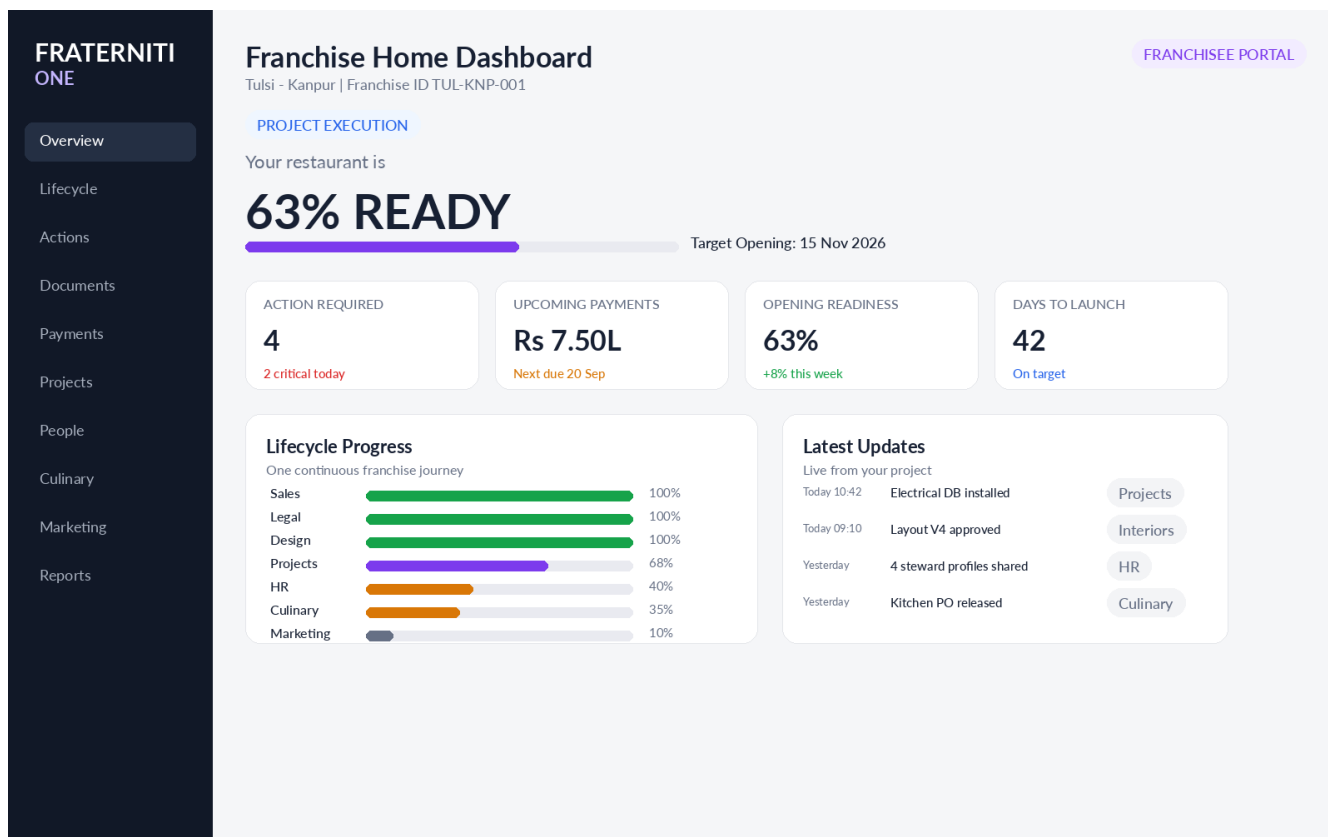


Implementation Notes

All dashboard cards deep-link to filtered detail views. Current stage and target opening must be computed, not manually typed.

Wireframe 02 - Lifecycle Timeline

Stage-wise view with completion, current stage and upcoming handoffs.

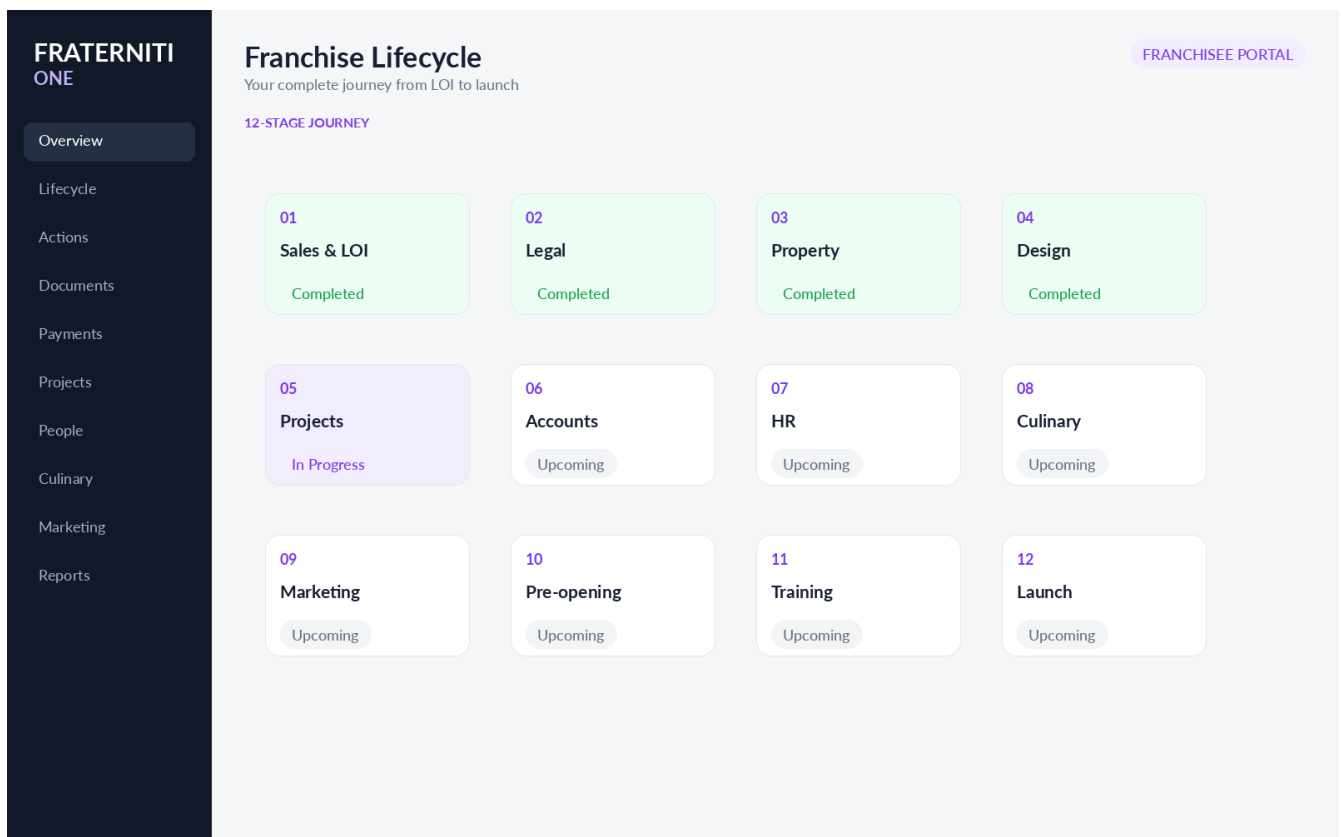

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 03 - Action Centre

Central queue for payments, documents, approvals and franchisee decisions.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Action Centre

Everything Fraterniti needs from the franchisee, in one place

CRITICAL

2

Due today

UPCOMING

5

Next 7 days

APPROVALS

3

Awaiting you

COMPLETED THIS WEEK

11

Great progress

Pending Actions

Sorted by urgency and project impact

Action	Owner	Type	Due	Priority
Pay kitchen equipment advance	Accounts	Rs 5,00,000	Today	Critical
Approve facade design V3	Interiors	Approval	Today	Critical
Upload GST certificate	Legal	Document	17 Sep	High
Select crockery option B/C	Culinary	Decision	18 Sep	Medium
Approve launch photoshoot	Marketing	Approval	20 Sep	Medium

Impact Summary

2 tasks currently block the opening timeline. Completing them today protects the target launch date.

2 BLOCKERS

3 APPROVALS

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 04 - Sales & Onboarding

LOI, commercial details, documents and sales-to-legal handoff.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Sales & Onboarding

Initial franchise handover and LOI record

FRANCHISEE PORTAL

FRANCHISE STATUS

Onboarded

Sales completed

FRANCHISE FEE

Rs 25.0L

Payment acknowledged

DIRECTOR APPROVAL

Approved

12 Sep 2026

Commercial Summary

Brand	Tulsi
Format	Premium Pure Veg
Territory	Kanpur, Uttar Pradesh
Sales Manager	Rahul
Director Approval	Karan / Rohit
Handover To	Legal Department

Documents

Letter of Intent	Signed	12 Sep
Payment Acknowledgement	Verified	12 Sep
Commercial Proposal	Final	11 Sep
KYC Pack	Received	12 Sep

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 05 - Legal & Compliance

Franchise, entity and property compliance workflow with legal sign-off.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Legal & Compliance

Compliance, agreements, property diligence and legal clearance

FRANCHISEE PORTAL

LEGAL READINESS

78%

3 items pending

FRANCHISE AGREEMENT

Signed

Leegality complete

LEASE REVIEW

In Review

Landlord changes

NACH

Pending

Franchisee action

Compliance Checklist


Item	Owner	Status	Due	Remarks
Franchise Agreement	Legal	Completed	12 Sep	-
Entity / KYC	Franchisee	Completed	12 Sep	-
Lease Deed	Legal	In Review	16 Sep	2 clauses
GST / PAN	Franchisee	Completed	13 Sep	-
NACH Mandate	Accounts + Legal	Pending	17 Sep	Action required
Signage Rights	Landlord	Pending	18 Sep	Dependency

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 06 - Interiors & Design

Design versions, approvals, drawings and BOQ lifecycle.

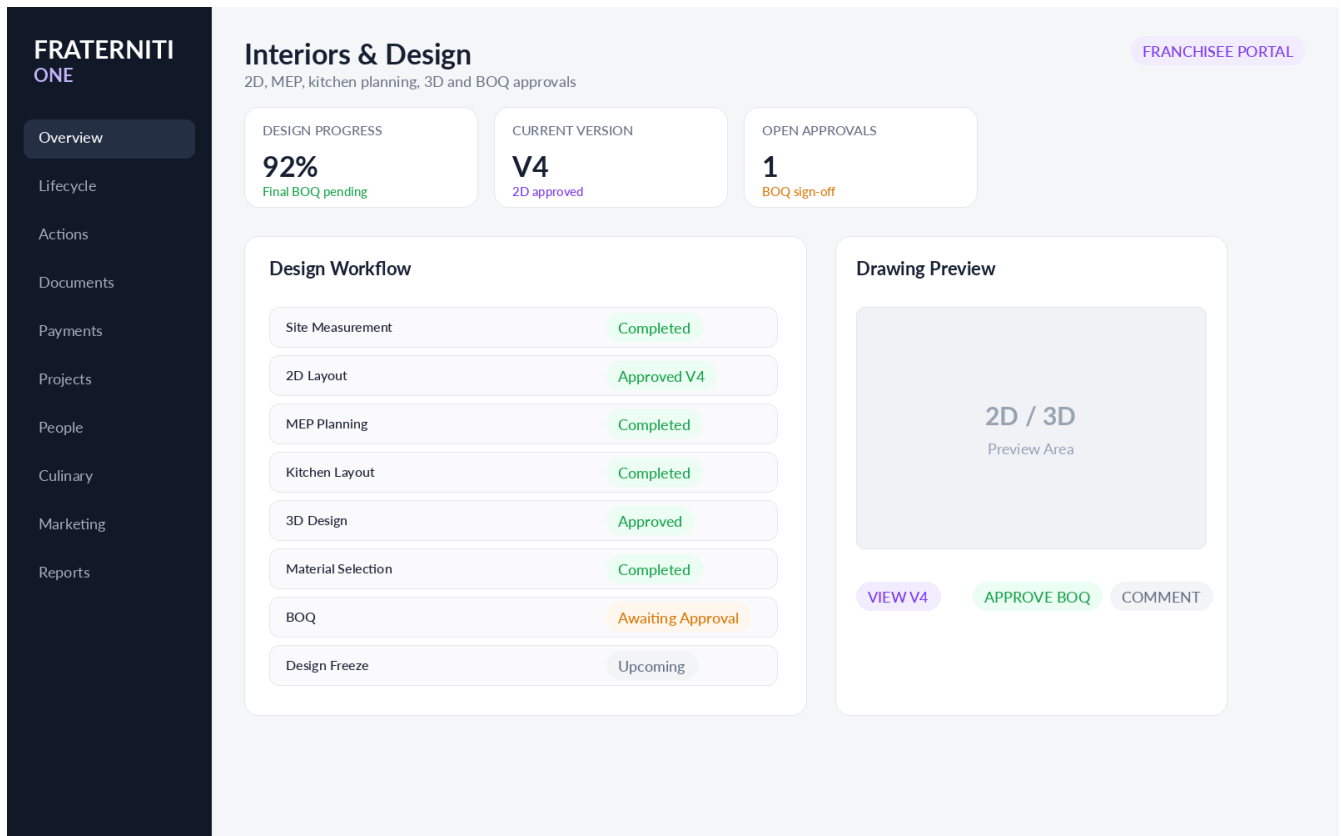

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 07 - Project Execution

Construction work packages, vendors, progress, issues and target dates.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Project Execution

On-ground construction, installation and handover

FRANCHISEE PORTAL

SITE PROGRESS

68%

+6% this week

DELAY

0 Days

On schedule

ACTIVE VENDORS

8

3 on site today

OPEN ISSUES

3

1 critical

Work Package Progress

Package	Progress	Status	Start	Target
Civil Work	100%	Completed	05 Sep	06 Sep
Electrical	85%	In Progress	08 Sep	18 Sep
Plumbing	90%	In Progress	08 Sep	17 Sep
HVAC	60%	In Progress	10 Sep	22 Sep
Flooring	55%	In Progress	12 Sep	24 Sep
Kitchen Install	40%	In Progress	14 Sep	28 Sep
Furniture	20%	Started	15 Sep	02 Oct
Facade	10%	Started	15 Sep	03 Oct

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 08 - Daily Site Report

Live construction DPR with progress, manpower, photos, completed work and next-day plan.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Daily Site Report

15 September 2026 | Live project reporting

FRANCHISEE PORTAL

TODAY PROGRESS

+1.8%

68% overall

MANPOWER ON SITE

34

8 teams

PHOTOS UPLOADED

18

Geo/time stamped

SAFETY / BLOCKERS

1

Escalation open

Today Completed

- Electrical DB installation completed
- Kitchen drainage line pressure-tested
- HVAC ducting zone A completed
- Ceiling grid work started
- Facade frame measurement confirmed

Tomorrow Plan

HVAC zone B, wall finish inspection, furniture marking and kitchen equipment base preparation.

Live Site Photo Feed

SITE PHOTO

10:40 AM

SITE PHOTO

11:41 AM

SITE PHOTO

12:40 AM

SITE PHOTO

13:41 AM

Implementation Notes

DPR submission should create timeline events and update work-package progress only within authorised limits.

Wireframe 09 - Accounts & Payments

Payment milestones, due dates, invoices, receipts and CRM reminders.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Accounts & Payments

CRM-led payment schedule, dues, invoices and receipts

FRANCHISEE PORTAL

TOTAL PROJECT VALUE

Rs 1.82Cr

Budgeted

PAID

Rs 1.11Cr

61%

UPCOMING 7 DAYS

Rs 12.5L

3 payments

OVERDUE

Rs 2.5L

1 critical

Payment Schedule

Purpose	Type	Amount	Due	Status
Kitchen Equipment	Vendor PO	Rs 5,00,000	15 Sep	Due Today
Furniture	Advance	Rs 2,50,000	18 Sep	Upcoming
HVAC	Milestone 2	Rs 3,00,000	20 Sep	Upcoming
Launch Marketing	Advance	Rs 2,00,000	25 Sep	Planned
Franchise Fee	Final tranche	Rs 2,50,000	12 Sep	Overdue

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 10 - HR & Manpower

Role-wise hiring, salary planning, joining dates and readiness.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

HR & Manpower

Hiring plan, salary budget, joining and training readiness

FRANCHISEE PORTAL

PLANNED HEADCOUNT

32

Store opening team

HIRED

21

66% complete

MONTHLY PAYROLL

Rs 6.05L

Budget Rs 6.20L

PENDING

11

4 priority hires

Manpower Plan

Role	Req.	Hired	Monthly Cost	Joining	Status
Restaurant Manager	1	1	Rs 45,000	10 Oct	Ready
Head Chef	1	1	Rs 55,000	05 Oct	Ready
CDP	3	2	Rs 90,000	08 Oct	Hiring
Commis	8	5	Rs 1,60,000	10 Oct	Hiring
Stewards	12	8	Rs 1,92,000	12 Oct	Hiring
Cashier	2	2	Rs 44,000	10 Oct	Ready

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 11 - Culinary & Menu

Culinary selections, equipment, menu, ingredients, training and trials.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Culinary & Menu

Menu, equipment, smallwares, ingredients and food trials

FRANCHISEE PORTAL

CULINARY READINESS

72%

5 workstreams active

MENU

Approved

84 items

EQUIPMENT

Ordered

ETA 28 Sep

FOOD TRIAL

08 Oct

Upcoming

Culinary Workstreams


Workstream	Owner	Status	Output / Next
Menu Finalisation	Corporate Chef	Completed	84 items
Recipe Standardisation	R&D	Completed	Version 2.1
Kitchen Equipment	Procurement	Ordered	ETA 28 Sep
Crockery	Franchisee + Culinary	Selection Pending	2 options
Cutlery / Glassware	Culinary	Finalised	PO next
Ingredient Mapping	Supply Chain	In Progress	72%
Chef Training	Training	Upcoming	01-07 Oct
Food Trials	Corporate Chef	Upcoming	08 Oct

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 12 - Procurement Tracker

Vendor-level PO, advance, dispatch, delivery and installation visibility.

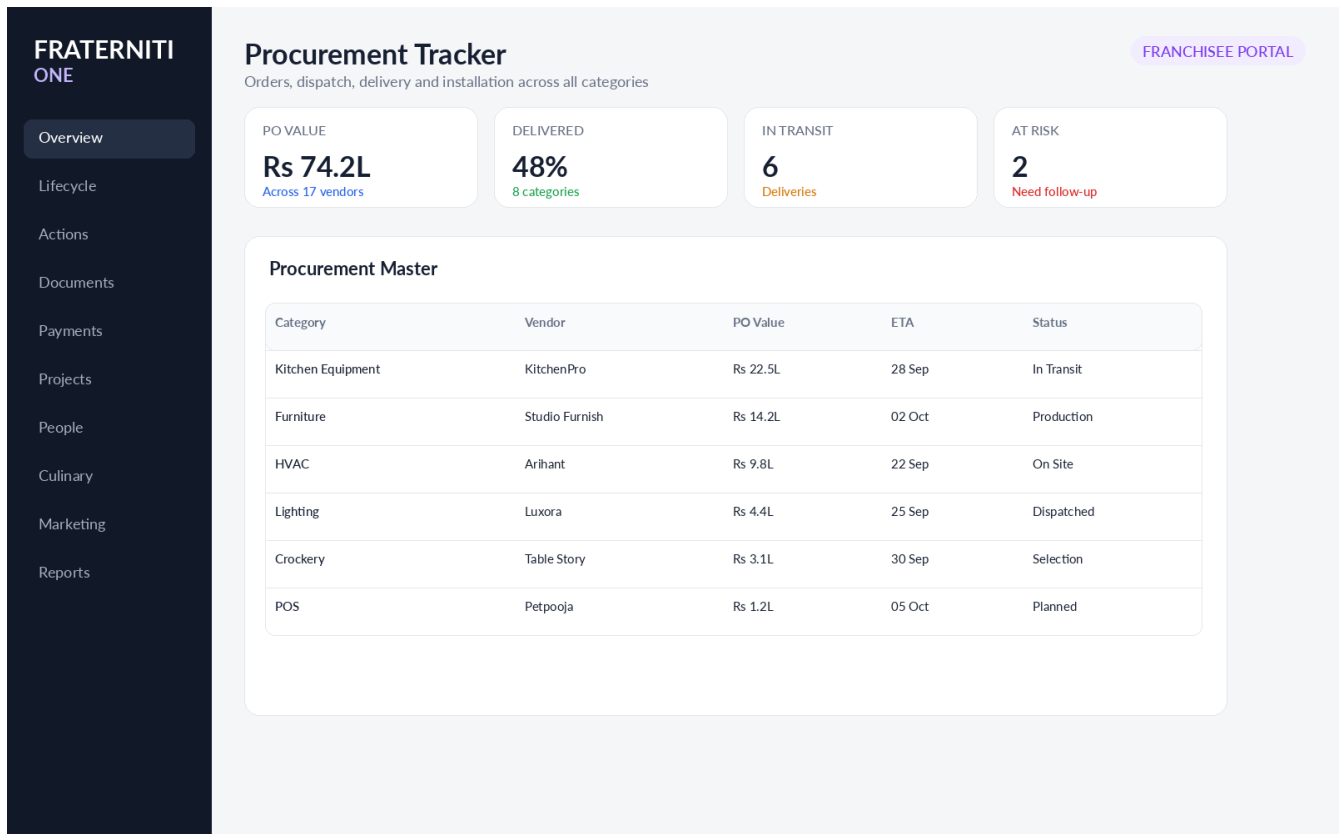

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 13 - Marketing & Launch

Pre-launch marketing calendar, asset approvals and launch readiness.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Marketing & Launch

Pre-launch demand creation, content, influencers and launch execution

FRANCHISEE PORTAL

MARKETING READINESS

45%

Launch plan active

LAUNCH DATE

15 Nov

61 days

INFLUENCERS

18

Shortlisted

ASSETS READY

12 / 28

Brand + local

Launch Marketing Plan

Activity	Channel	Status	Target
Google Business Profile	Digital	In Progress	20 Sep
Instagram Local Handle	Social	Completed	14 Sep
Photoshoot	Content	Planned	25 Oct
Influencer Outreach	PR	In Progress	01 Nov
Meta Launch Campaign	Performance	Planned	05 Nov
Outdoor / Local	Local Marketing	Planned	06 Nov
Grand Launch Event	Events	Planned	15 Nov

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 14 - Pre-Opening Readiness

Cross-department readiness score and critical blockers before opening.



Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 15 - Training & Certification

Training assignments, assessments, certificates and opening eligibility.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Training & Certification

Owner, manager, service, kitchen, POS and SOP readiness

FRANCHISEE PORTAL

TEAM TRAINING

61%

24 / 39 complete

AVG SCORE

84%

Pass mark 75%

CERTIFIED

18

Opening eligible

RE-TEST

3

Due this week

Training Matrix

Module	Audience	Status	Score	Next
Owner Orientation	Owner	Completed	92%	Certified
Manager SOP	Restaurant Manager	Completed	88%	Certified
Service Training	FOH Team	In Progress	81%	24 Sep
Kitchen SOP	BOH Team	In Progress	86%	28 Sep
POS / Billing	Cashier + Manager	Upcoming	-	02 Oct
Opening Drill	All Staff	Upcoming	-	10 Nov

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 16 - Grand Opening Control Room

Final sign-offs, launch-day checklist, team and event readiness.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Grand Opening Control Room

Final go-live approval and launch-day command centre

FRANCHISEE PORTAL

GO-LIVE STATUS

READY

All sign-offs green

OPENING

15 Nov

12:00 PM

TEAM ON DUTY

38

Full roster

GUEST / MEDIA

126

Confirmed

Department Sign-Offs

Legal

Approved

Projects

Approved

Accounts

Approved

HR

Approved

Culinary

Approved

Marketing

Approved

Operations

Approved

Launch Day Checklist

Final inventory count

POS live test

Staff briefing

Guest list desk

Influencer coordination

Photography / video

Opening offer activated


Management command group

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 17 - Communication Centre

Department threads linked to project tasks, approvals and files.

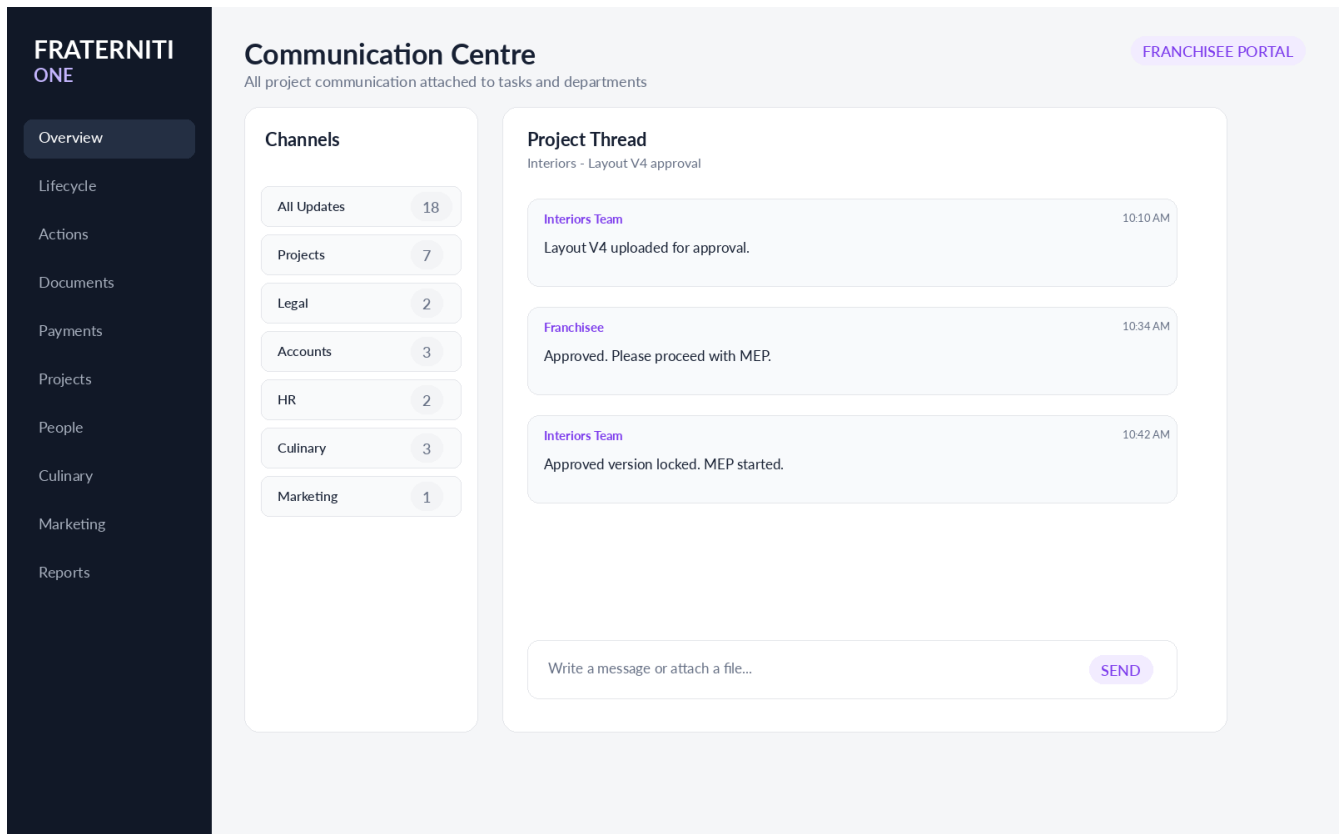

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 18 - Document Vault

Version-controlled documents grouped by lifecycle module and department.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Document Vault

Single source of truth for every project document

FRANCHISEE PORTAL

TOTAL FILES

86

12 categories

APPROVED

71

Latest versions

AWAITING

7

Review / signature

STORAGE

1.8 GB

Project archive

Project Files


Folder	Contents	Files	Last Activity
Sales	LOI, proposal, receipts	8	Updated 12 Sep
Legal	Agreement, lease, KYC, NACH	17	Updated today
Interiors	2D, 3D, MEP, BOQ	22	Updated today
Projects	POs, site reports, snag list	14	Updated today
Accounts	Invoices, receipts, ledger	11	Updated today
HR	Manpower plan, offers	6	Updated yesterday
Culinary	Menu, recipes, equipment	8	Updated today

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 19 - Management Command Centre

Portfolio view for management: stage, readiness, opening date, health and ownership.

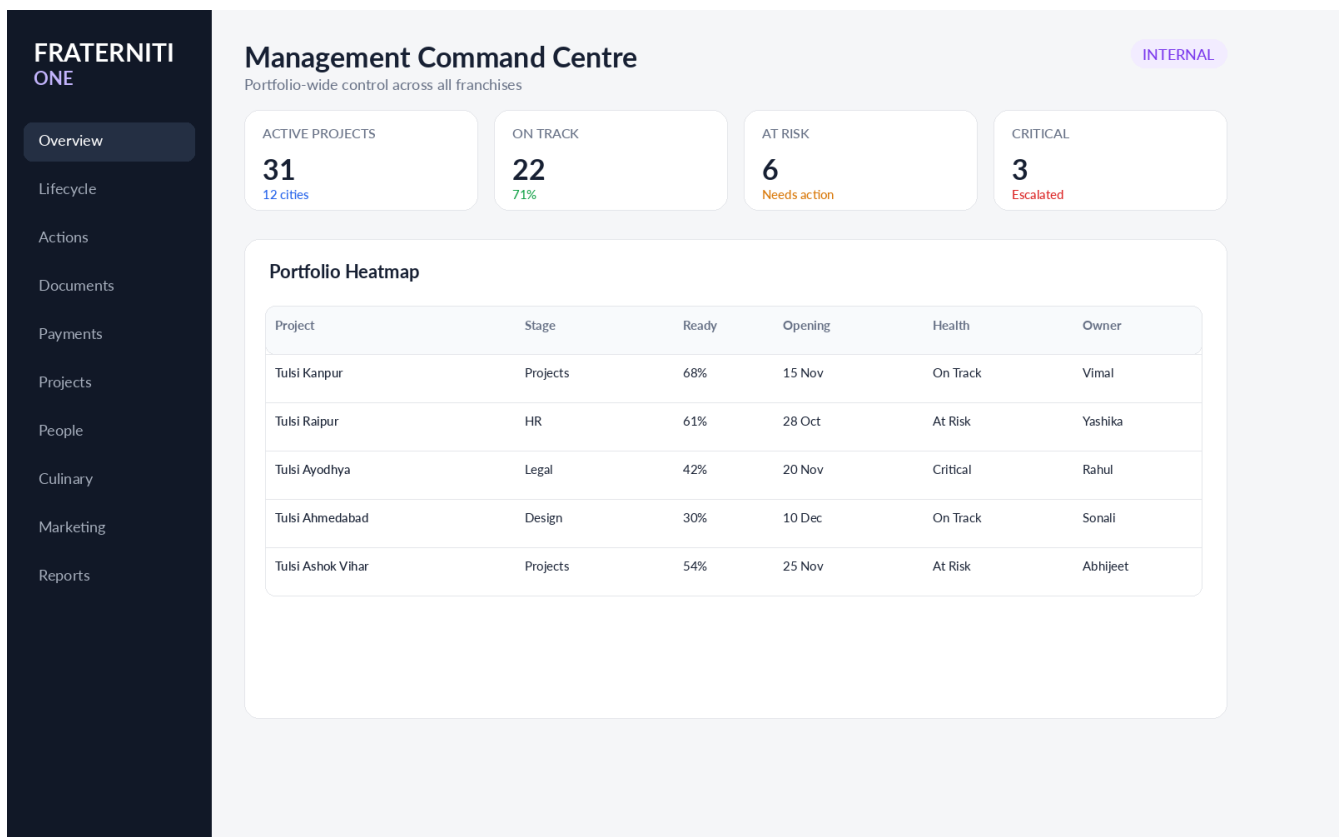

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 20 - Live Reporting Command Centre

Real-time feed, reporting compliance, blockers and cross-department reporting controls.



Implementation Notes

This is the central internal event stream and reporting-compliance view; filters by brand, city, project, department and severity are required.

Wireframe 21 - Department Status Matrix

Cross-functional project status with owner, due date, dependency and health.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Department Status Matrix

One project, all department statuses and dependencies

INTERNAL

Tulsi Kanpur - Cross Functional Matrix


Department	Progress	Current Task	Owner	Due	Dependency	Health
Sales	100%	Handover complete	Rahul	Done	-	Green
Legal	78%	Lease review	Legal	17 Sep	Landlord	Amber
Interiors	92%	BOQ sign-off	Design	16 Sep	Franchisee	Amber
Projects	68%	HVAC + flooring	PM	22 Sep	BOQ	Green
Accounts	61%	Kitchen payment	Accounts	15 Sep	Franchisee	Red
HR	66%	BOH hiring	HR	30 Sep	Budget	Amber
Culinary	72%	Crockery select	Chef	18 Sep	Franchisee	Amber
Marketing	45%	GBP setup	Marketing	20 Sep	Location	Green

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 22 - Delay & Dependency Tracker

Critical-path blockers, ownership, aging and opening-date impact.

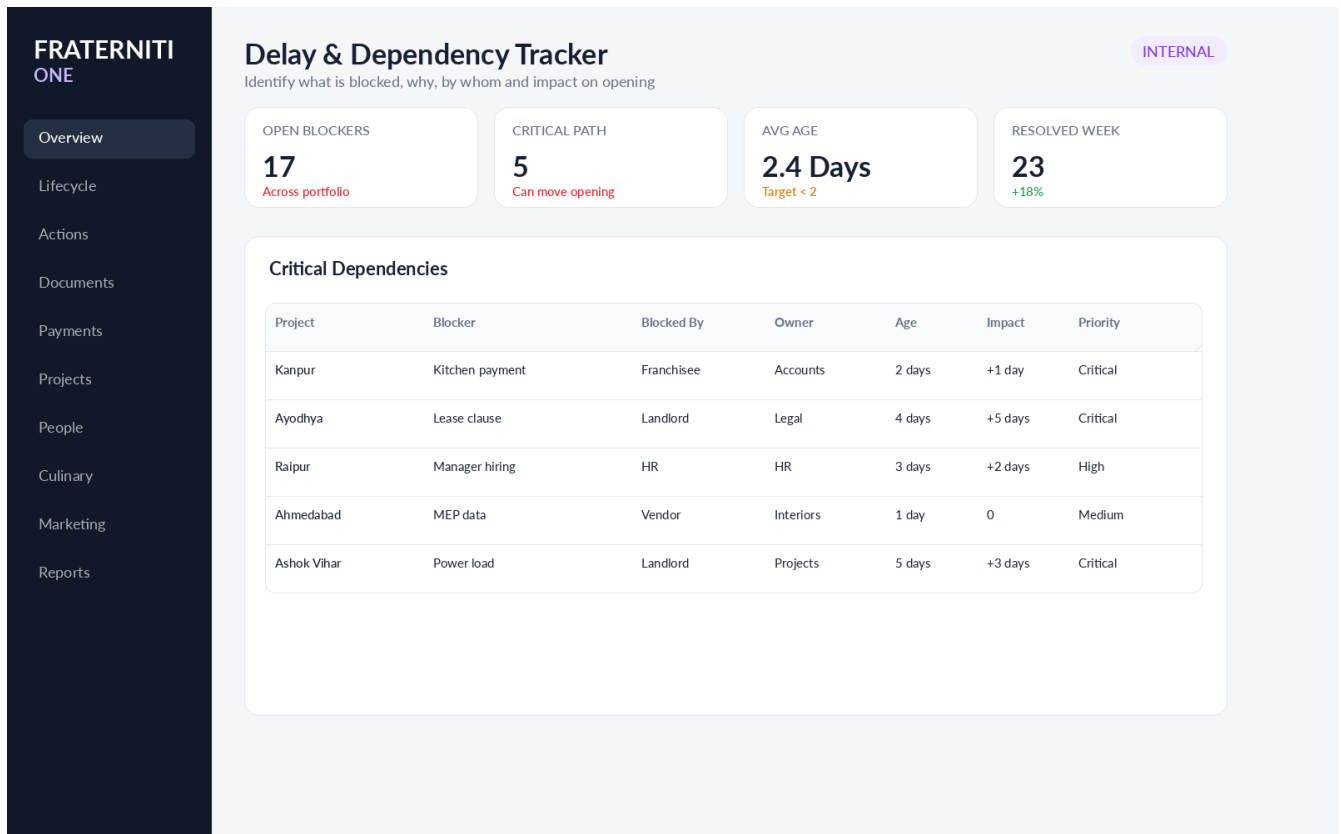


Implementation Notes

Opening impact should be manually estimable at first; later forecasting can become rules-based from critical path data.

Wireframe 23 - Milestone & SLA Analytics

Stage-wise SLA performance, reporting compliance and escalation rules.

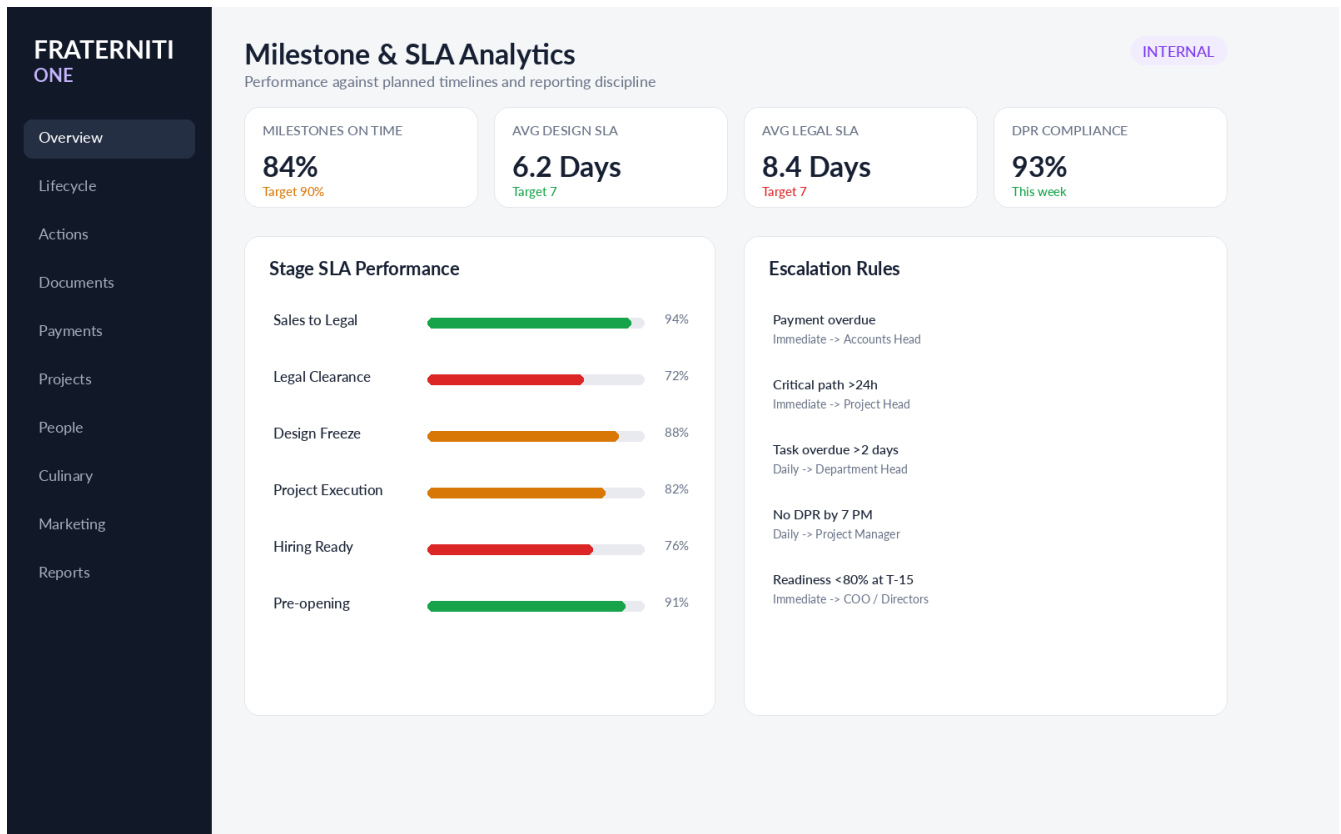

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 24 - Activity & Audit Log

Full traceability for user actions, approvals, edits and system events.

FRATERNITI
ONE

Overview

Lifecycle

Actions

Documents

Payments

Projects

People

Culinary

Marketing

Reports

Activity & Audit Log

Immutable history of approvals, edits, payments and status changes

INTERNAL

Project Activity Log

Filter by project, department, user, action or date


Time	Department	Actor	Action	Reference
15 Sep 10:42	Interiors	Apoorv	Layout V4 marked Approved	Version V4
15 Sep 10:35	Accounts	CRM	Payment receipt verified	Rs 5,00,000
15 Sep 10:21	Projects	Site PM	Electrical progress 80 -> 85%	Photo proof
15 Sep 09:50	Legal	Legal Team	Lease clause escalated	Clause 14.2
14 Sep 18:55	HR	HR Manager	Candidate offer accepted	Restaurant Manager
14 Sep 16:10	Culinary	Corporate Chef	Menu version locked	Menu V2.1

Implementation Notes

Filters, search, attachment previews and role-based actions should be available where relevant. All data changes must preserve project ID and audit context.

Wireframe 25 - Mobile Franchise Views

Responsive quick views for owner actions, site updates and opening readiness.

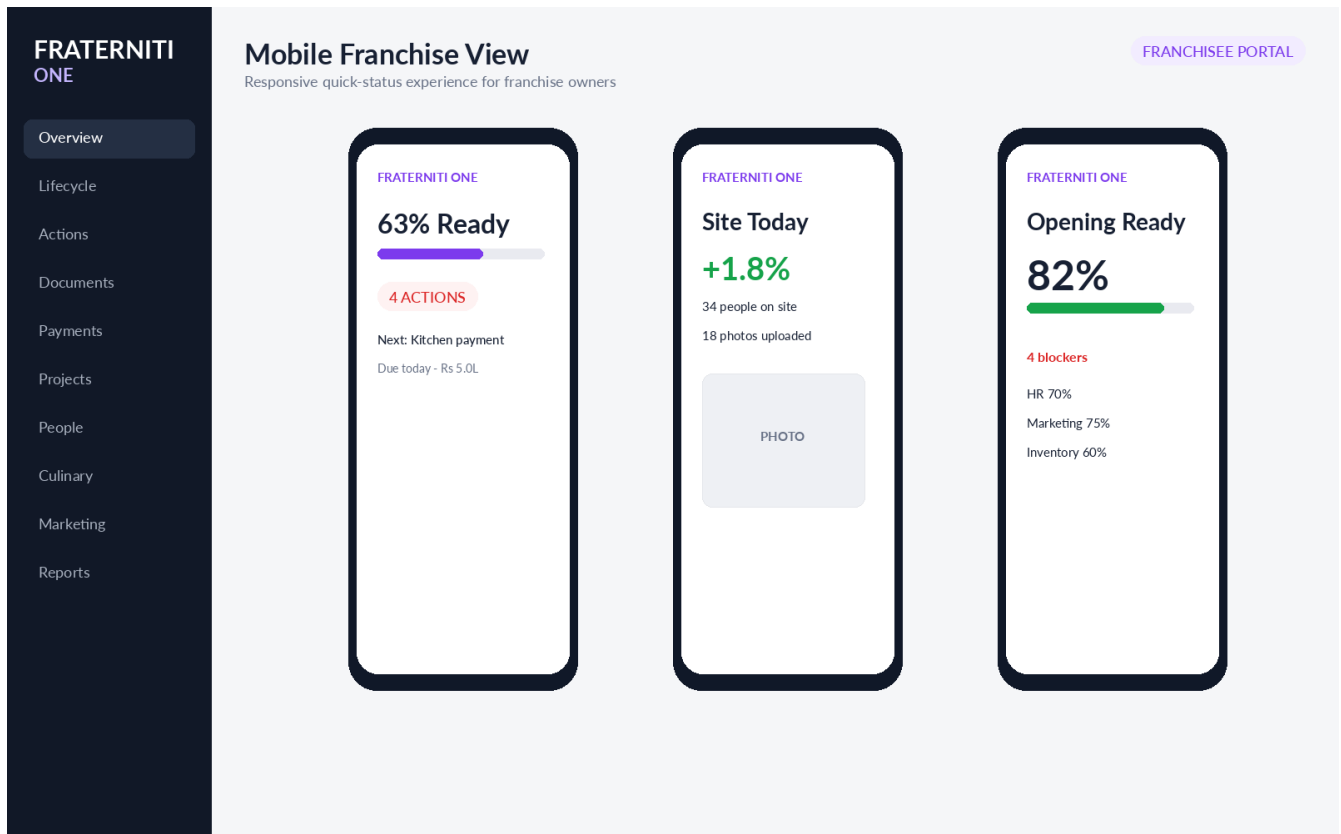

Implementation Notes

Mobile prioritises actions, today status, approvals, payments and readiness rather than reproducing every desktop table.

18. Handoff Notes for Apoorv

- Build the shared data model and workflow engine before polishing individual department screens.
- Do not implement each department as a standalone mini-app with duplicate project/franchise data.
- Every screen should read/write through Project ID, Task/Approval IDs and consistent status masters.
- Treat opening date, readiness and critical blockers as first-class product objects.
- Design versioning, finance verification and audit logs should be designed early; retrofitting these later is expensive.
- Keep checklist/workflow templates configurable so Tulsi, Zoca and future brands can differ without separate codebases.
- Use feature flags/configuration to roll out modules gradually.

Definition of done for the product design phase

Apoorv should be able to take this document and convert each wireframe into clickable UI, define backend models/routes for the listed entities, estimate development module-by-module, and identify only implementation-level questions rather than re-discovering the business workflow.
